
P6 PROGRAMME HEALTH CHECK – DASHBOARD


P6 SETTINGS	SCHEDULE QUALITY & INTEGRITY	CRITICAL-KEY ITEMS (YES)	TO RECHECK & RESUBMIT	OVERALL HEALTH SCORE	HEALTH RATING
100.0%	76.0%	20	0	80.8%	ACCEPTABLE
20.0 of 20.0 units	60.8 of 80.0 applicable units	20 passed | 0 other	7 Fail | 3 Warning | 0 N/A overall	80.8 of 100.0 applicable units	Critical gate: all critical items Pass ✓


SUBMISSION VERDICT: ACCEPTED WITH COMMENTS – no critical-key item to resubmit


PROJECT NAME	SCHEDULE TYPE	PROJECT START	PROJECT FINISH	DATA DATE	REVIEWER	REVIEW DATE
MAHSR C4 - CWP Baseline	Baseline	10-Dec-2020	08-Dec-2024	10-Dec-2020	Planning Engineer (P6)	14-Oct-2026


TOTAL ACTIVITIES	TOTAL WBS NODES	TOTAL RELATIONSHIPS	TOTAL RESOURCES	NEGATIVE FLOAT ACTIVITIES	CRITICAL PATH ACTIVITIES
6,078	1,979	13,094	431	0	1,343
6,078 incomplete	Work Breakdown Structure	FS 81% | FS Density 2.15	labor + nonlabor + material	0.0% of incomplete	22.1% of all activities

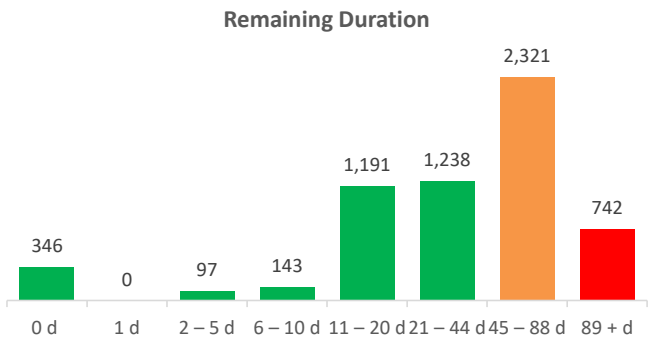


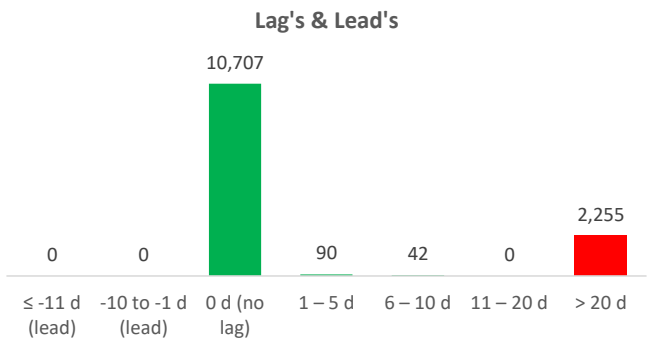

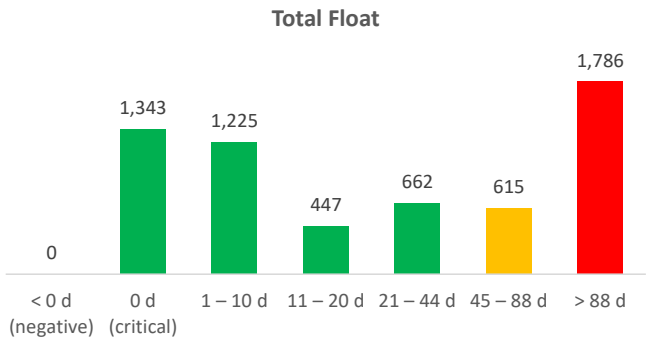

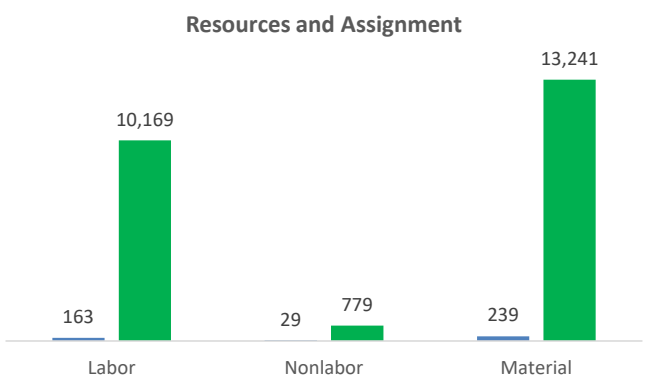

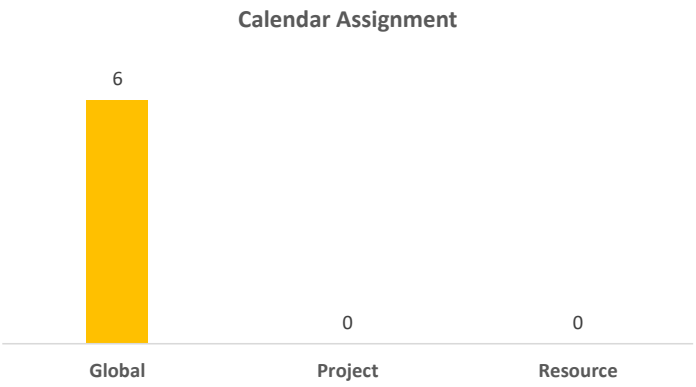

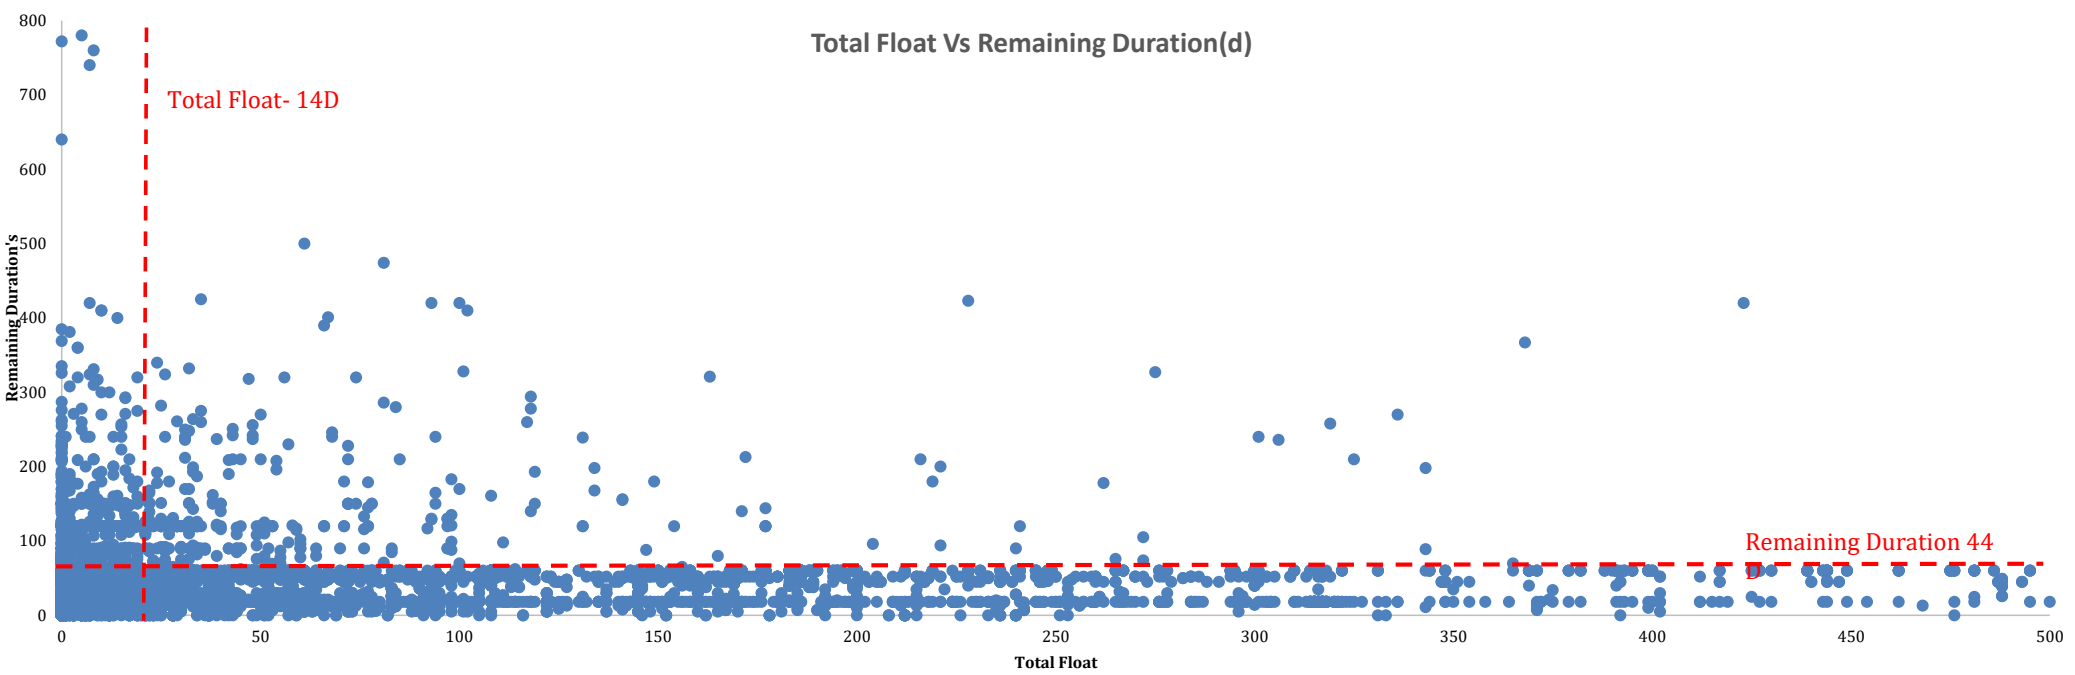

Sensitivity: LNT Construction Internal Use
